

AWARD COPY

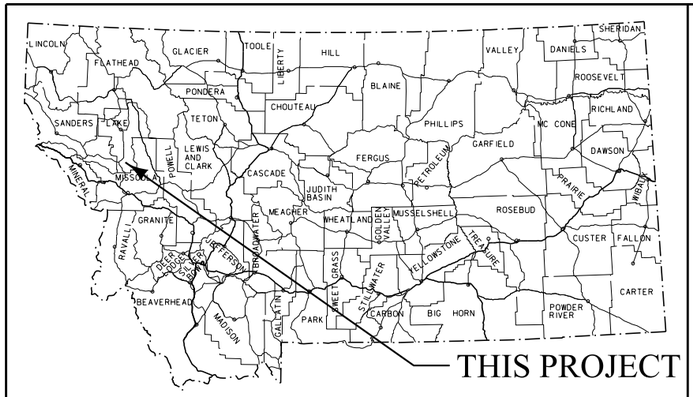

MONTANA DEPARTMENT OF TRANSPORTATION

FEDERAL AID PROJECT STPX 24(56)
AQUATIC RESOURCES MITIGATION
WS 3 - JOHNSON WETLAND MITIGATION
LAKE COUNTY
EROSION CONTROL PLAN

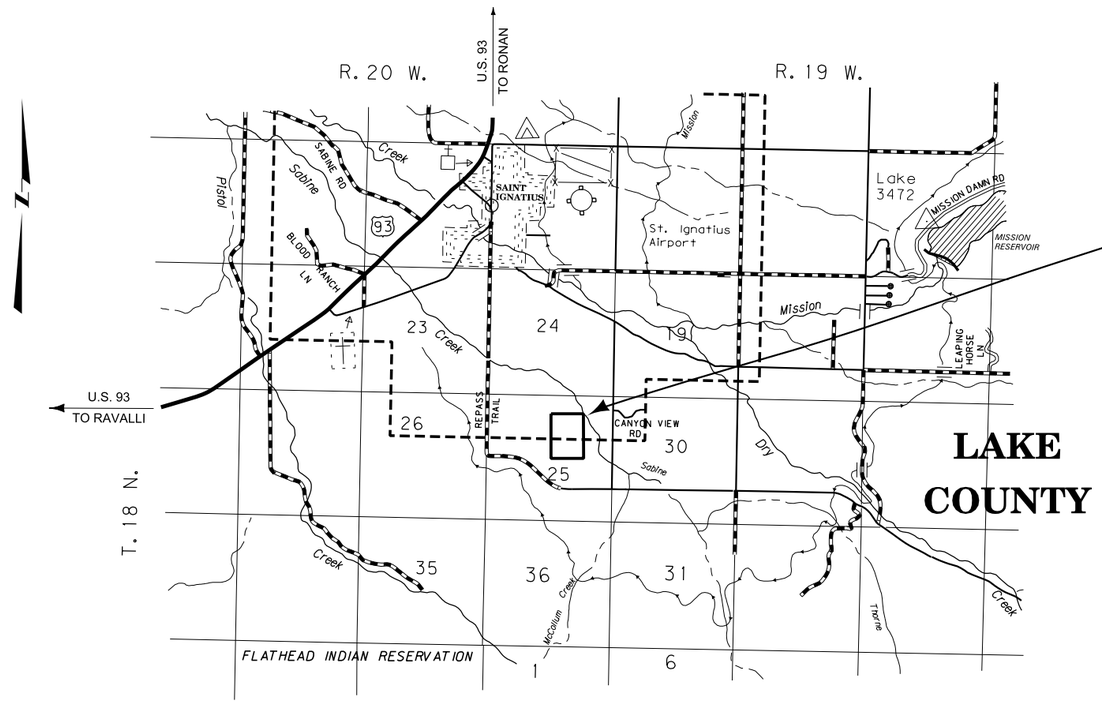

THIS CONTRACT
AQUATIC RESOURCES MITIGATION
STPX 24(56)

3	MDT MONTANA DEPARTMENT OF TRANSPORTATION	8583000RDERTZ01.dgn				EROSION CONTROL PLANS	
2		4/2/2024					
1		1:15:15 PM jmelson				UPN 8583000	

EROSION AND SEDIMENT CONTROL BMP'S

REFER TO THE MOST CURRENT RELEASE OF SECTION 208 OF THE DETAILED DRAWINGS

VBS (SS-14) AND PEV (SS-02) SHOULD BE IDENTIFIED AND USED THROUGHOUT THE ENTIRE PROJECT IN ALL AREAS NOT DISTURBED BY CONSTRUCTION

TS (SS-04) AND ES (SS-15) SHOULD BE UTILIZED THROUGHOUT THE ENTIRE PROJECT

GENERAL BMP'S

- I/O — INLET/OUTLET PROTECTION
- WP — WATERWAY PROTECTION
- WR — WATER RESOURCE PROTECTION

TEMPORARY SOIL STABILIZATION BMP'S (SS)

- PEV — PRESERVATION OF EXISTING VEGETATION (SS-2)
- HM — HYDRAULIC MULCH (SS-3)
- TS — TEMPORARY SEEDING (SS-4)
- SB — SOIL BINDERS (SS-5)
- SM — STRAW MULCH (SS-6)
- EC — EROSION CONTROL BLANKETS/MATS, PLASTIC COVERS, AND GEOTEXTILES. (SS-7)
- WM — WOOD MULCH (SS-8)
- ED — EARTH DIKES, DRAINAGE SWALES AND LINED DITCHES (SS-9)
- OP — OUTLET PROTECTION / VELOCITY DISSIPATION DEVICES (SS10)
- TSD — SLOPE DRAINS (SS-11)
- SR — SLOPE ROUGHENING (SS-12)
- GT — TERRACED SLOPES (SS-13)
- VBS — VEGETATED BUFFER (SS-14)
- ES — EROSION SEEDING (SS-15)

WIND EROSION CONTROL BMP'S (WE)

- WE-1 — WIND EROSION CONTROL

TEMPORARY SEDIMENT CONTROL BMP'S (SC)

- SF — SILT FENCE (SC-1)
- DB — DESILTING BASIN (SC-2)
- ST — SEDIMENT TRAP (SC-3)
- CD — CHECK DAMS (SC-4)
- FR — FIBER ROLLS (SC-5)
- GBB — GRAVEL BAG BERM (SC-6)
- SAND-B — SAND BAG BARRIERS (SC-8)
- STRAW-B — STRAW BALE BARRIERS (SC9)
- SDP — STORM DRAIN INLET PROTECTION (SC-10)
- DDB — DUGOUT DITCH BASIN (SC-11)

TRACKING CONTROL BMP'S (TC)

- SCEE — STABILIZED CONSTRUCTION ENTRANCE/EXIT (TC-1)
- EETW — ENTRANCE/EXIT TIRE WASH (TC-3)

THE FOLLOWING BMP ALTERNATIVES ARE NOT COMPREHENSIVE AND DO NOT SUPERSEDE MDT STANDARD SPECIFICATIONS OR MANDATES AND REQUIREMENTS SPECIFIED BY OTHER AUTHORIZED STATE AND FEDERAL AGENCIES.

I/O INLET/OUTLET PROTECTION*

OP, FR, ST, DB, SF, CD, SDP, GBB, SAND-B, STRAW-B, EC

WP WATERWAY PROTECTION*

VBS, FR, SF, SR, GBB, HM, CD, SAND-B, STRAW-B

WR WATER RESOURCE PROTECTION*

VBS, FR, SF, EC, SR, GBB, HM, CD, SAND-B, STRAW-B

DT DITCH TREATMENT*

DDB, CD, ST, ED, GBB, SAND-B, STRAW-B, EC, SM, FR, HM


NOTE: BMP STATIONING IS APPROXIMATE

CONSTRUCTION LIMITS:
CUT SECTION
TOE OF FILL

AWARD COPY

T. 18. N. R. 19 W.

SEC. 25

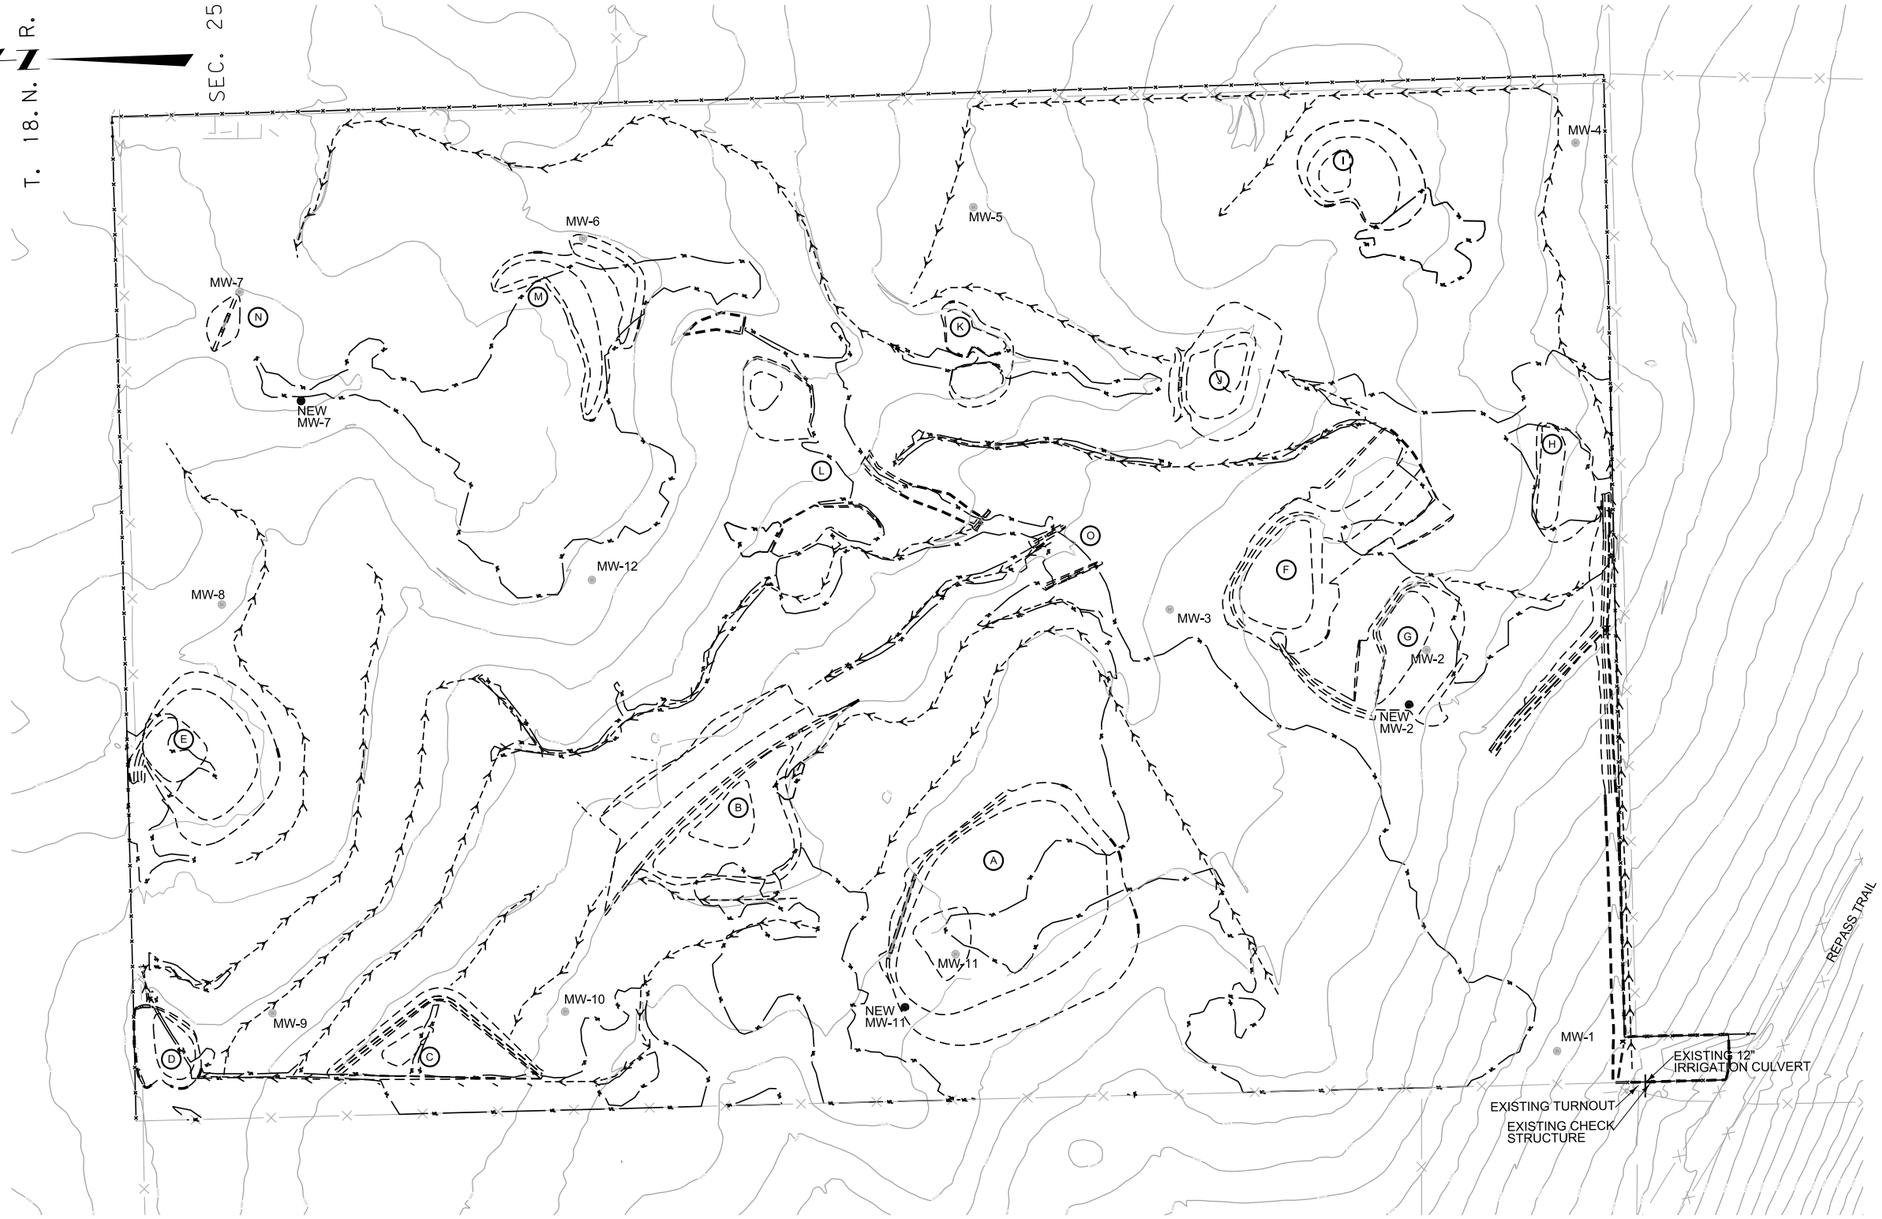

LEGEND

- VEGETATED SPILLWAY
- IRRIGATION FEATURE
- MONITORING WELL/ GEOTECHNICAL BORING
- (A) WETLAND CELL ID
- NEW WILDLIFE FRIENDLY FENCE
- WL EXISTING WETLAND
- EXISTING SPREADER DITCHES

3	MDT MONTANA DEPARTMENT OF TRANSPORTATION	8583000RDEROZ01.dgn				EROSION CONTROL PLANS		WS 3 - JOHNSON WETLAND MITIGATION	STPX 24(56)
2		4/2/2024							
1		1:15:19 PM jrnelson				LAKE COUNTY		UPN 8583000	SHEET 3
